

DVCS Meeting


Aug 23, 2010

Weekly Progress

Installation

- Calorimeter restacked (see photo)
- ARS / Calo Trigger Rack moved to HRS Detector Hut
 - Cable patch panel in place in hut.
- Concrete wall for next to HRS-R (under construction)
 - HV cables in process, lay under HRS
- Jack Segal on vacation until 2 Sept.
- Mounting plaque for Low Voltage supply in shop
- RG213 patch panel installed on DVCS Stand
 - RG213-BNC adapters in Hall. cables sorted, laid out on floor.
 - Some cable carts found.
- Blue Light assembly delivered by shop

Restack

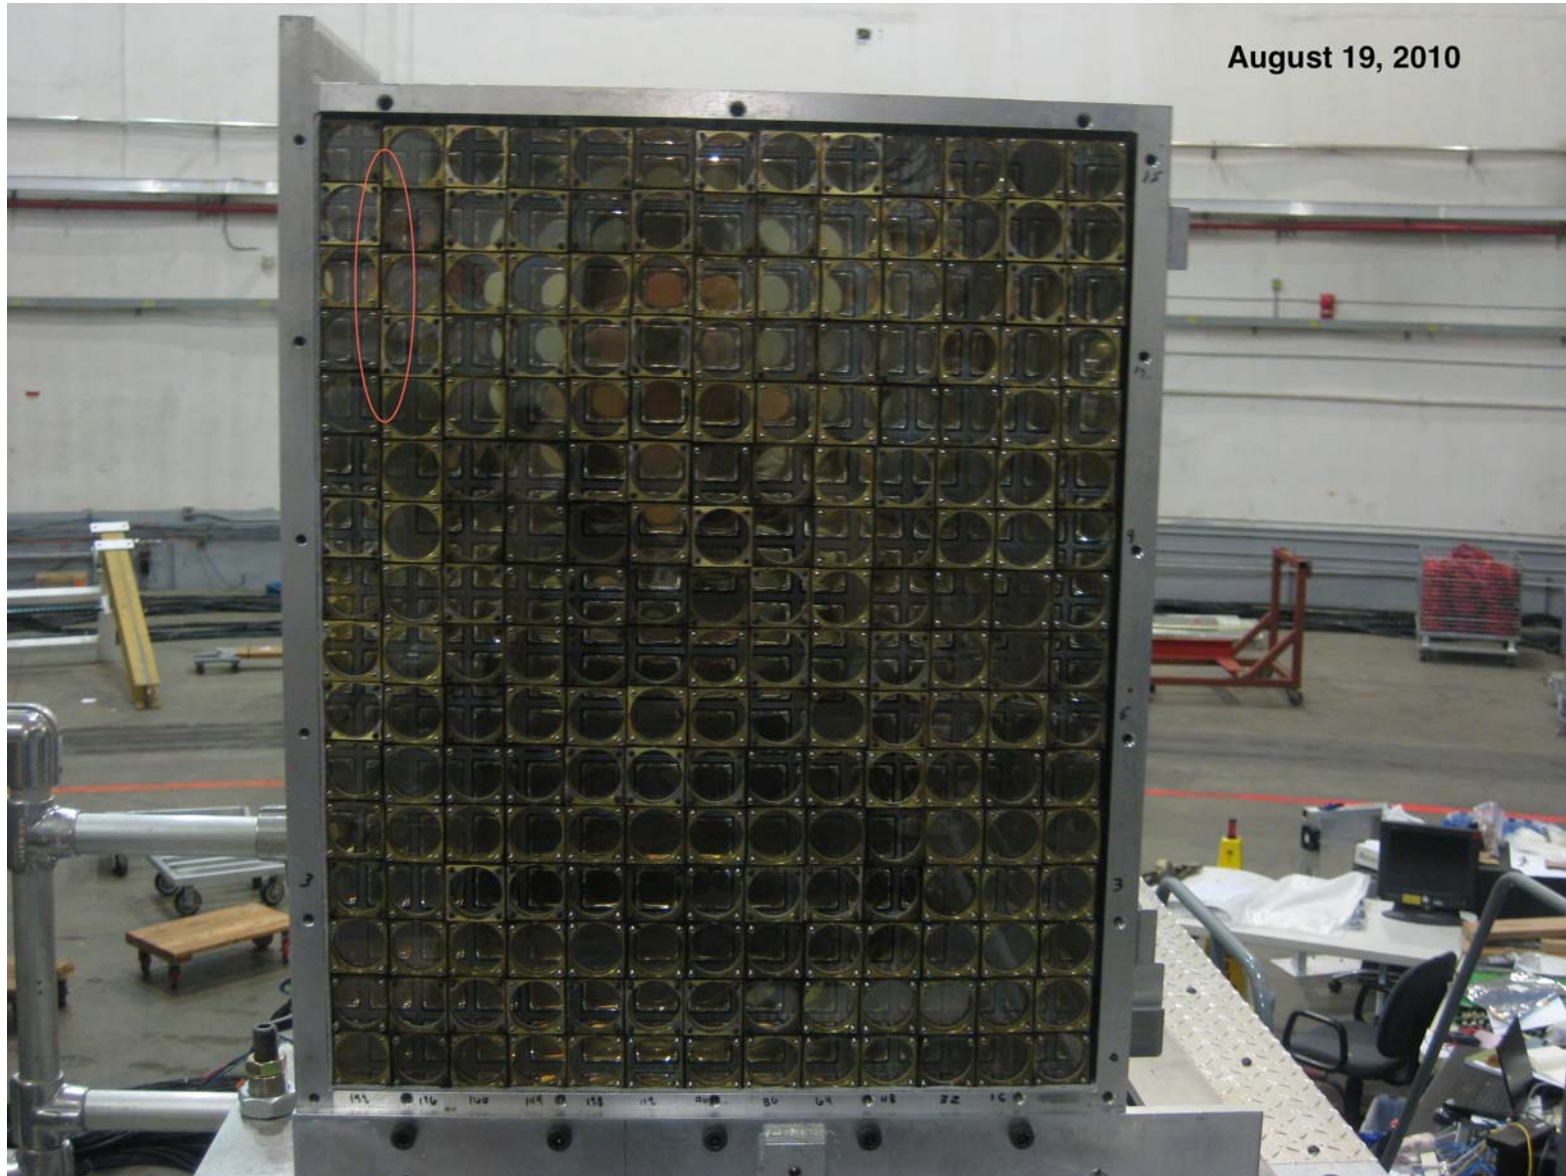

Program for Week

- Survey Calorimeter?
 - Ed will stack Pb Bricks before removing supporting jack.
- Ed Folts: RG-213 cables to hut patch?
- Install HV cables
- Reinstall Low Voltage power supply
 - Notify RADCON before work inside perimeter.
 - Beam pipe is 200 mr/hr
- Re-connect DAQ in HRS hut
- Build Blue Light assembly
- M. Crouau arrives
 - Connect ADC cables
 - Connect LED to VME card
