
EEI Cleanroom Update

02/02/2021 Malinga, Thir, Sean, and Anu

Cosmic data we took last week

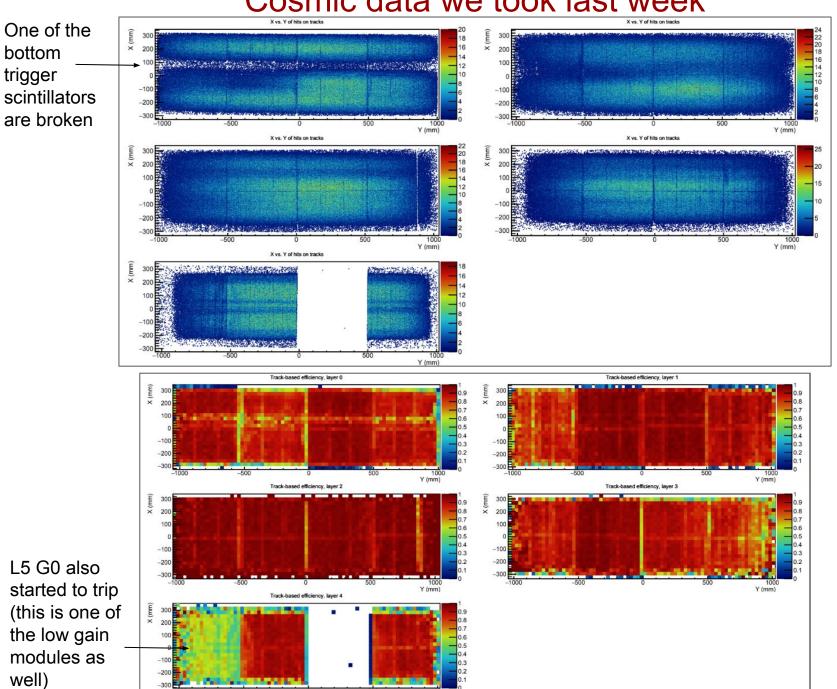

Additional things and plans for this week

- Layer #1 HV test was completed and all the 4 modules held the HV perfectly for over 12 hours at 4200 V equivalent (3742 V); so this layer is now ready for the cosmic stand
- Assembly of the layer #2 (8th layer to be assembled) is ongoing and we should be done in a fre days. With this layer completed, we only have 3 more layers to assemble
- Need to plan on moving the layer #5 out of the cosmic stand asap and apply the 85 % divider to those modules as those are currently the only ones without it. Will probably be done after Kondo is back

